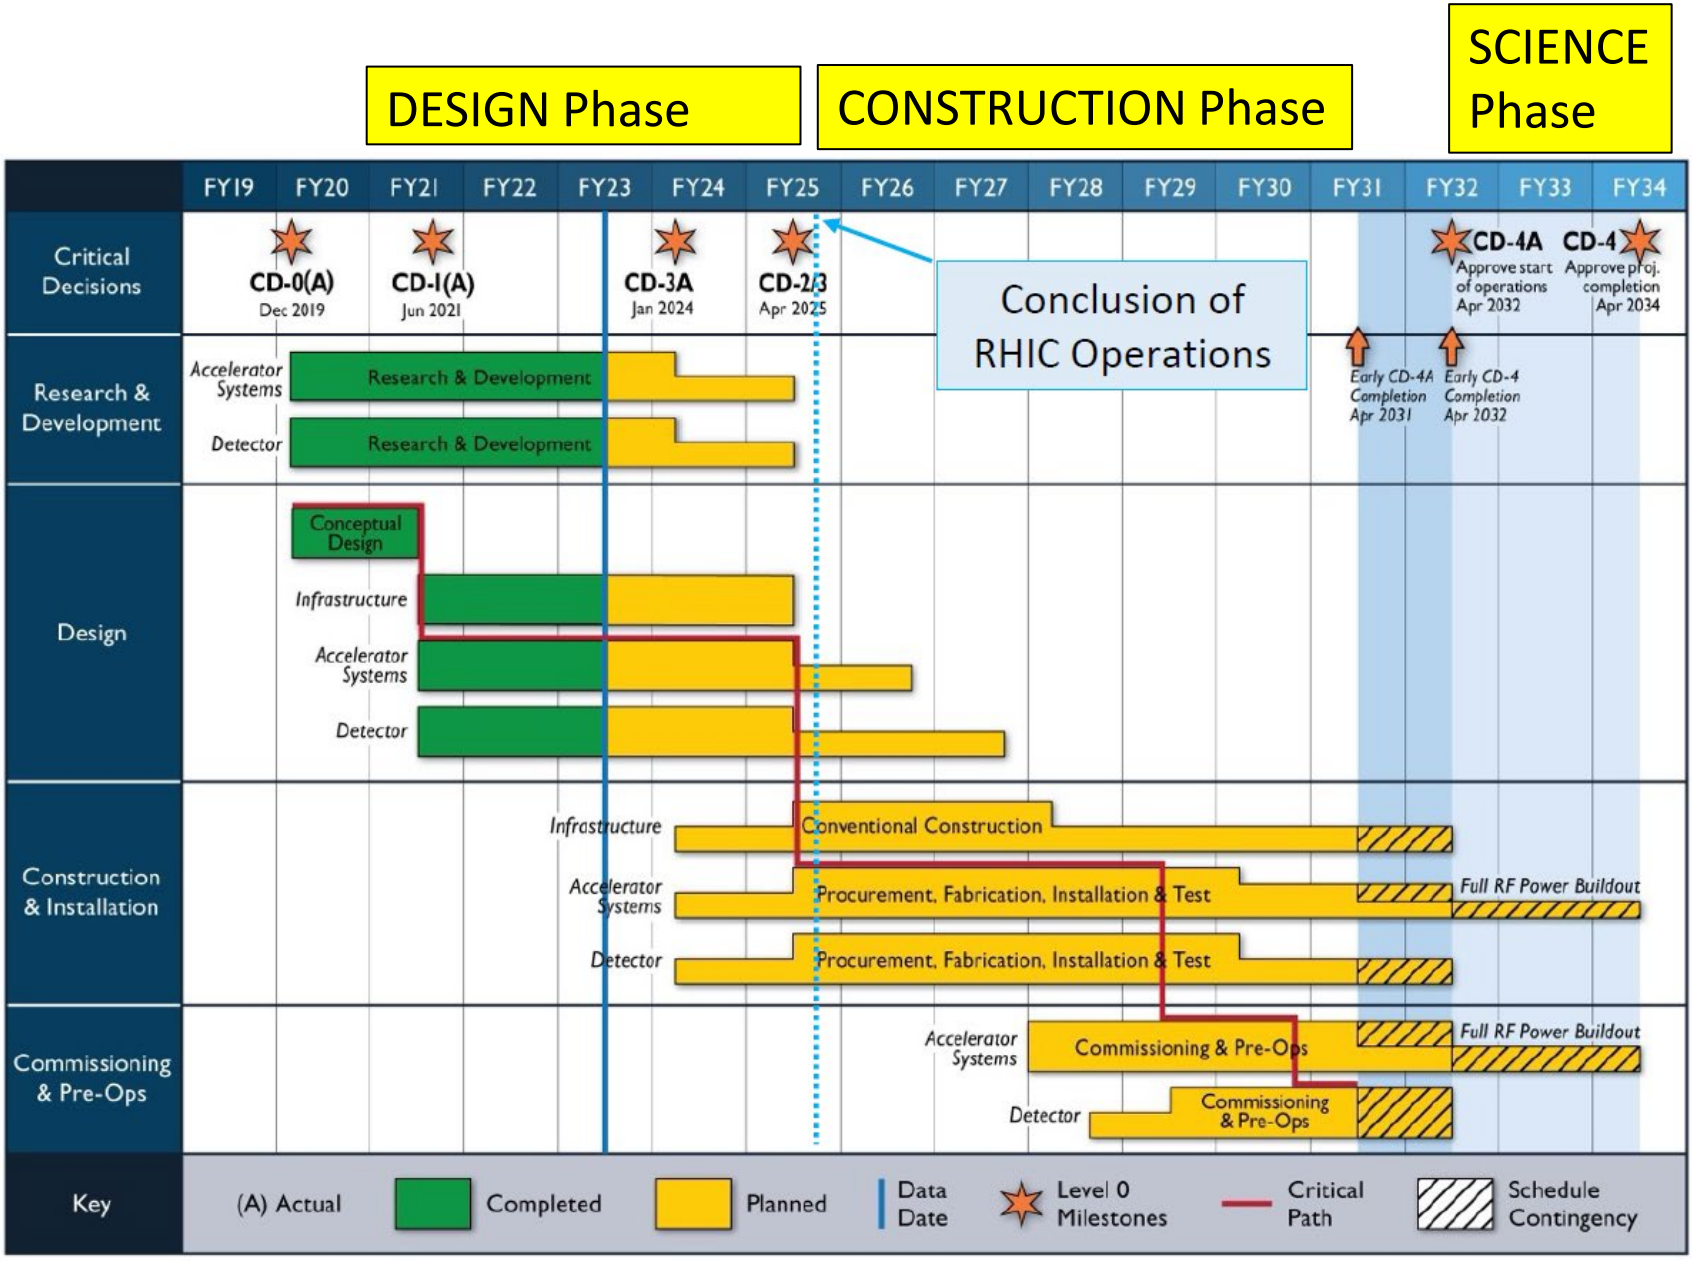
DESIGN Phase
CONSTRUCTION Phase
SCIENCE Phase
FY19
FY20
FY21
FY22
FY23
FY24
FY25
FY26
FY27
FY28
FY29
FY30
FY31
FY32
FY33
FY34
Critical Decisions
CD-0(A)
Dec 2019
CD-1(A)
Jun 2021
CD-3A
Jan 2024
CD-2/3
Apr 2025
CD-4A
Approve start of operations
Apr 2032
CD-4
Approve proj. completion
Apr 2034
Conclusion of RHIC Operations
Research & Development
Accelerator Systems
Research & Development
Detector
Research & Development
Early CD-4A Completion Apr 2031
Early CD-4 Completion Apr 2032
Design
Conceptual Design
Infrastructure
Accelerator Systems
Detector
Construction & Installation
Infrastructure
Conventional Construction
Accelerator Systems
Procurement, Fabrication, Installation & Test
Full RF Power Buildout
Detector
Procurement, Fabrication, Installation & Test
Commissioning & Pre-Ops
Accelerator Systems
Commissioning & Pre-Ops
Full RF Power Buildout
Detector
Commissioning & Pre-Ops
Key
(A) Actual
Completed
Planned
Data Date
Level 0 Milestones
Critical Path
Schedule Contingency
