





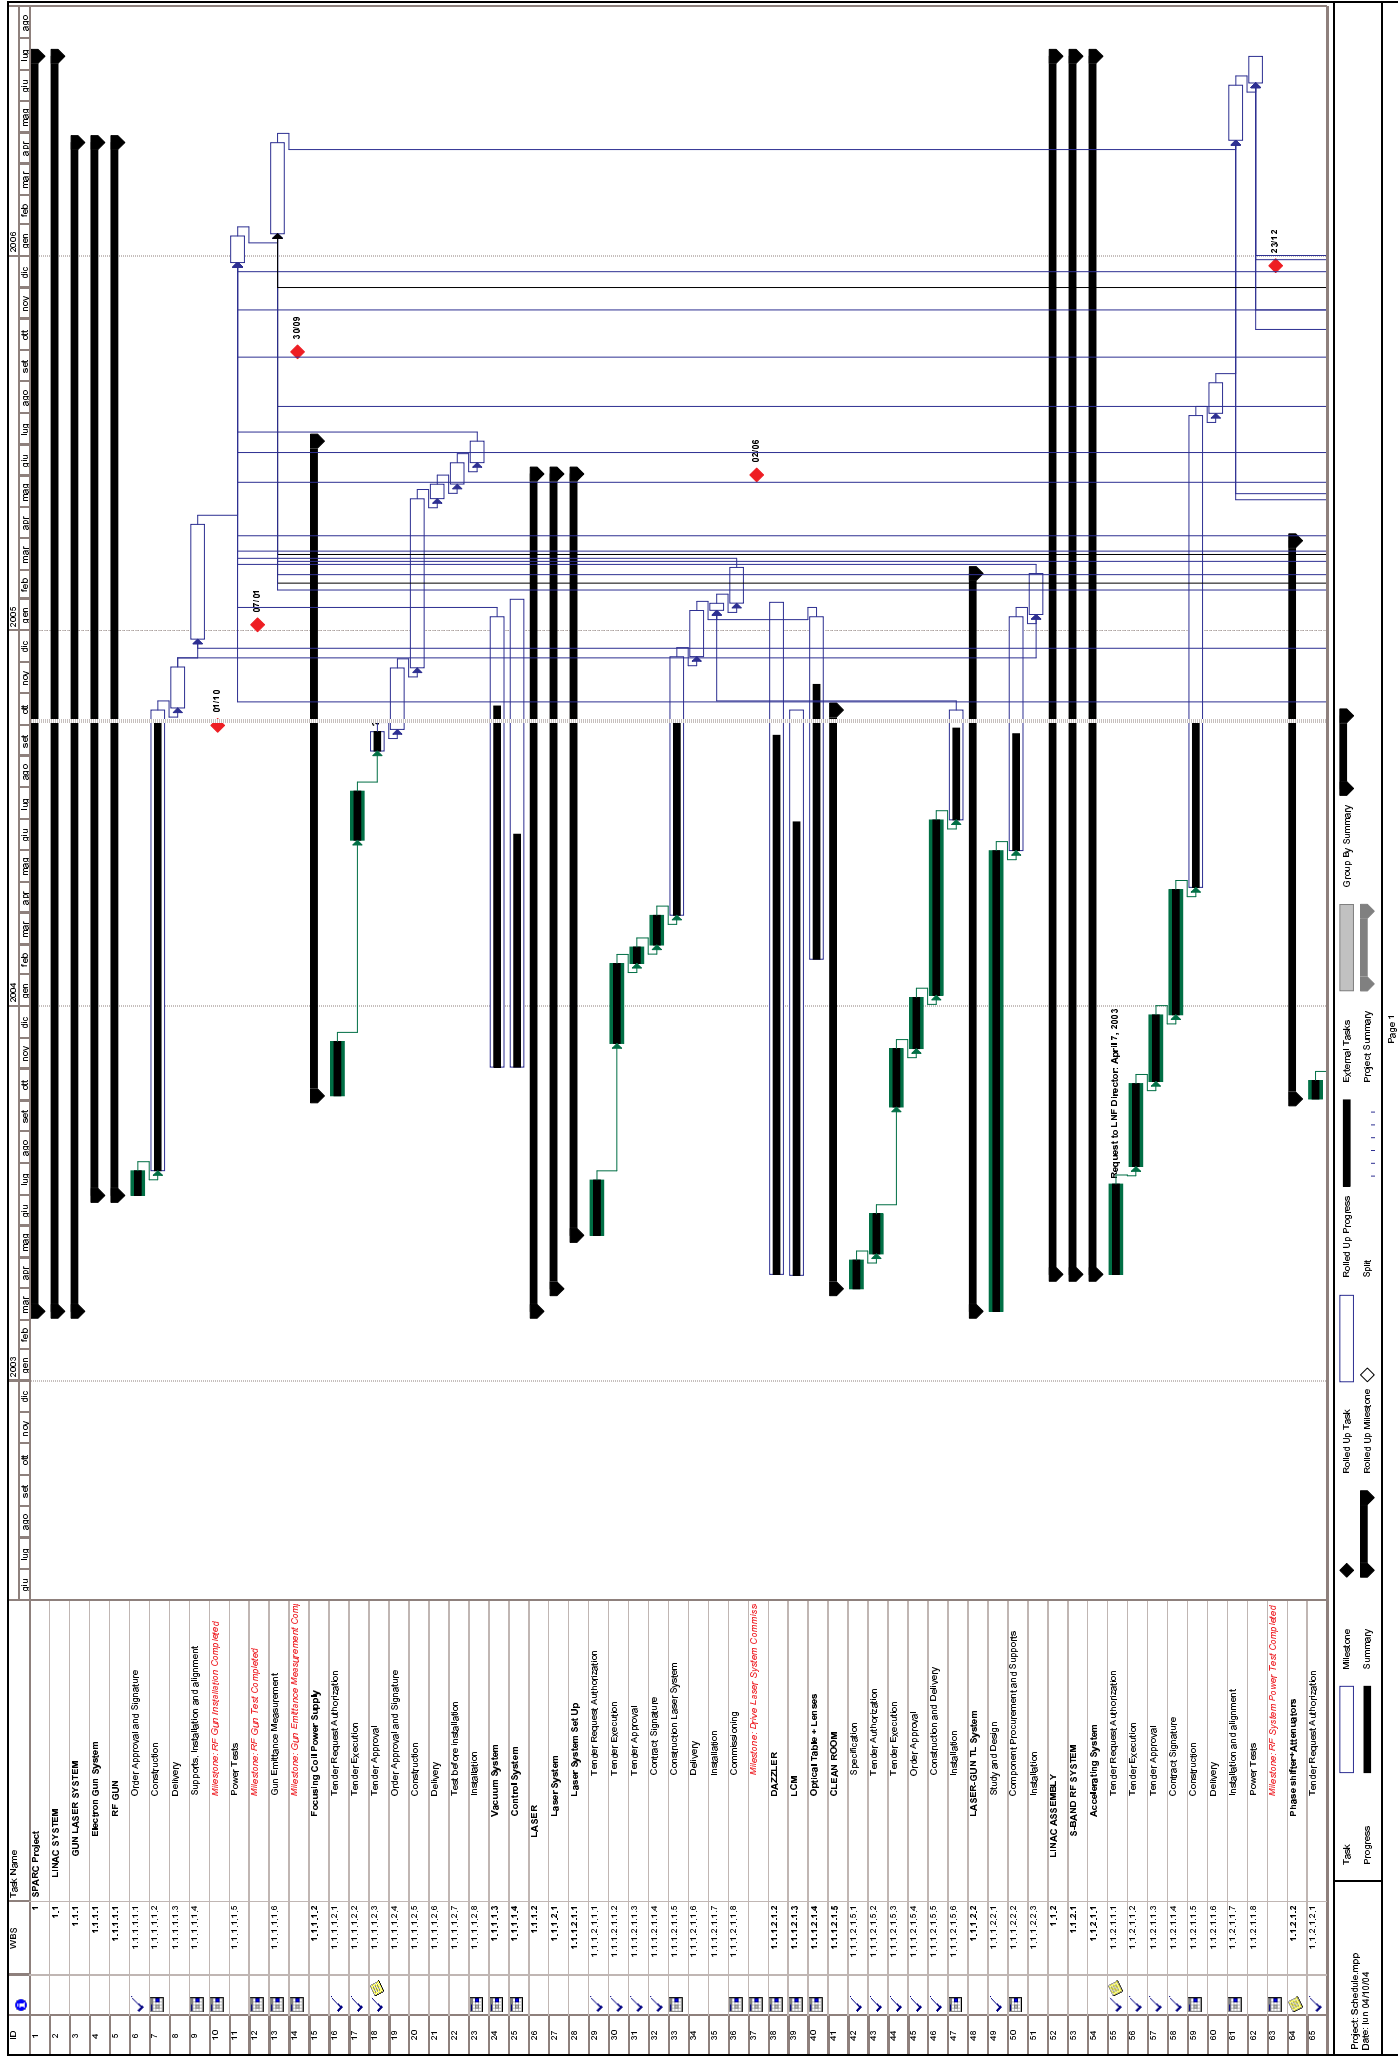

ID	WBS	Task Name	2003	2004	2005	2006
131	1.1.4.6	Valve Supports				
132	1.1.4.7	Vacuum Portable Equipments				
133	1.1.4.8	Insulation				
134	1.1.5	BEAM DIAGNOSTIC				
135	1.1.5.1	FLUORESCENT SCREENS				
136	1.1.5.2	ENERGY DEFINING DV/GE (Emitance Res. Dev)				
137	1.1.5.2.1	Mechanics and Vacuum				
138	1.1.5.2.1.1	Design				
139	1.1.5.2.1.2	Tender and Order				
140	1.1.5.2.1.3	Construction				
141	1.1.5.2.1.4	Window Tests				
142	1.1.5.2.2	Flag and Movement Drivers				
143	1.1.5.2.2.1	Design				
144	1.1.5.2.2.2	Tender and Order				
145	1.1.5.2.2.3	Construction				
146	1.1.5.2.3	Optical System and TV Camera				
147	1.1.5.2.3.1	Design				
148	1.1.5.2.3.2	Tender and Order				
149	1.1.5.2.3.3	Construction				
150	1.1.5.2.4	DAQ and Control System				
151	1.1.5.2.4.1	Design				
152	1.1.5.2.4.2	Tender and Order				
153	1.1.5.2.4.3	Construction				
154	1.1.5.2.5	Software and Analysis				
155		Alignment, Emittance Meas. Dev. Installing				
156	1.1.5.3	OTR				
157	1.1.5.3.1	Digital Camera				
158	1.1.5.3.1.1	Order for Camera				
159	1.1.5.3.1.2	Camera Software				
160	1.1.5.3.1.4	Installation and Tests				
161	1.1.5.3.1.3	Macro Lens				
162	1.1.5.3.3.1	Order				
163	1.1.5.3.3.2	Tests				
164	1.1.5.3.3.3	Tender and Order				
165	1.1.5.3.3.4	Construction				
166	1.1.5.3.5	Macro Lens Remote Control				
167	1.1.5.3.5.1	Design				
168	1.1.5.3.5.2	Tender and Order				
169	1.1.5.3.5.3	Construction				
170	1.1.5.3.7	Optical System				
171	1.1.5.3.7.1	Optical Components Order				
172	1.1.5.3.7.2	Design				
173	1.1.5.3.7.3	Tender and Order				
174	1.1.5.3.7.4	Construction				
175	1.1.5.4	FARADAY CUP				
176	1.1.5.5	WALL CURRENT MONITOR				
177	1.1.5.6	BPM-STRIP LINE				
178		Alignment, RF Deflector Power Tests				
179	1.1.5	COMPUTER CONTROL				
180	1.1.5.1	Console System				
181	1.1.5.1.1	Hardware and System Tests				
182		Hardware Orders				
183	1.1.5.1.2	Design and Tests				
184	1.1.5.2	e-LogBook				
185	1.1.5.2.1	Design and Tests				
186	1.1.5.2.2	Installation and Tests				
187	1.1.5.3	DAQ				
188	1.1.5.3.1	Prototype Tests				
189	1.1.5.3.2	Design				
190	1.1.5.3.3	Tender and Order				
191	1.1.5.3.4	Construction				
192	1.1.5.4	CABLES & TRAYS				
193	1.2	COMMON SERVICES				
194	1.2.1	PROCESS WATER AND AIR CONDITIONING SYSTEM				
195	1.2.1.1	Preliminary Design				

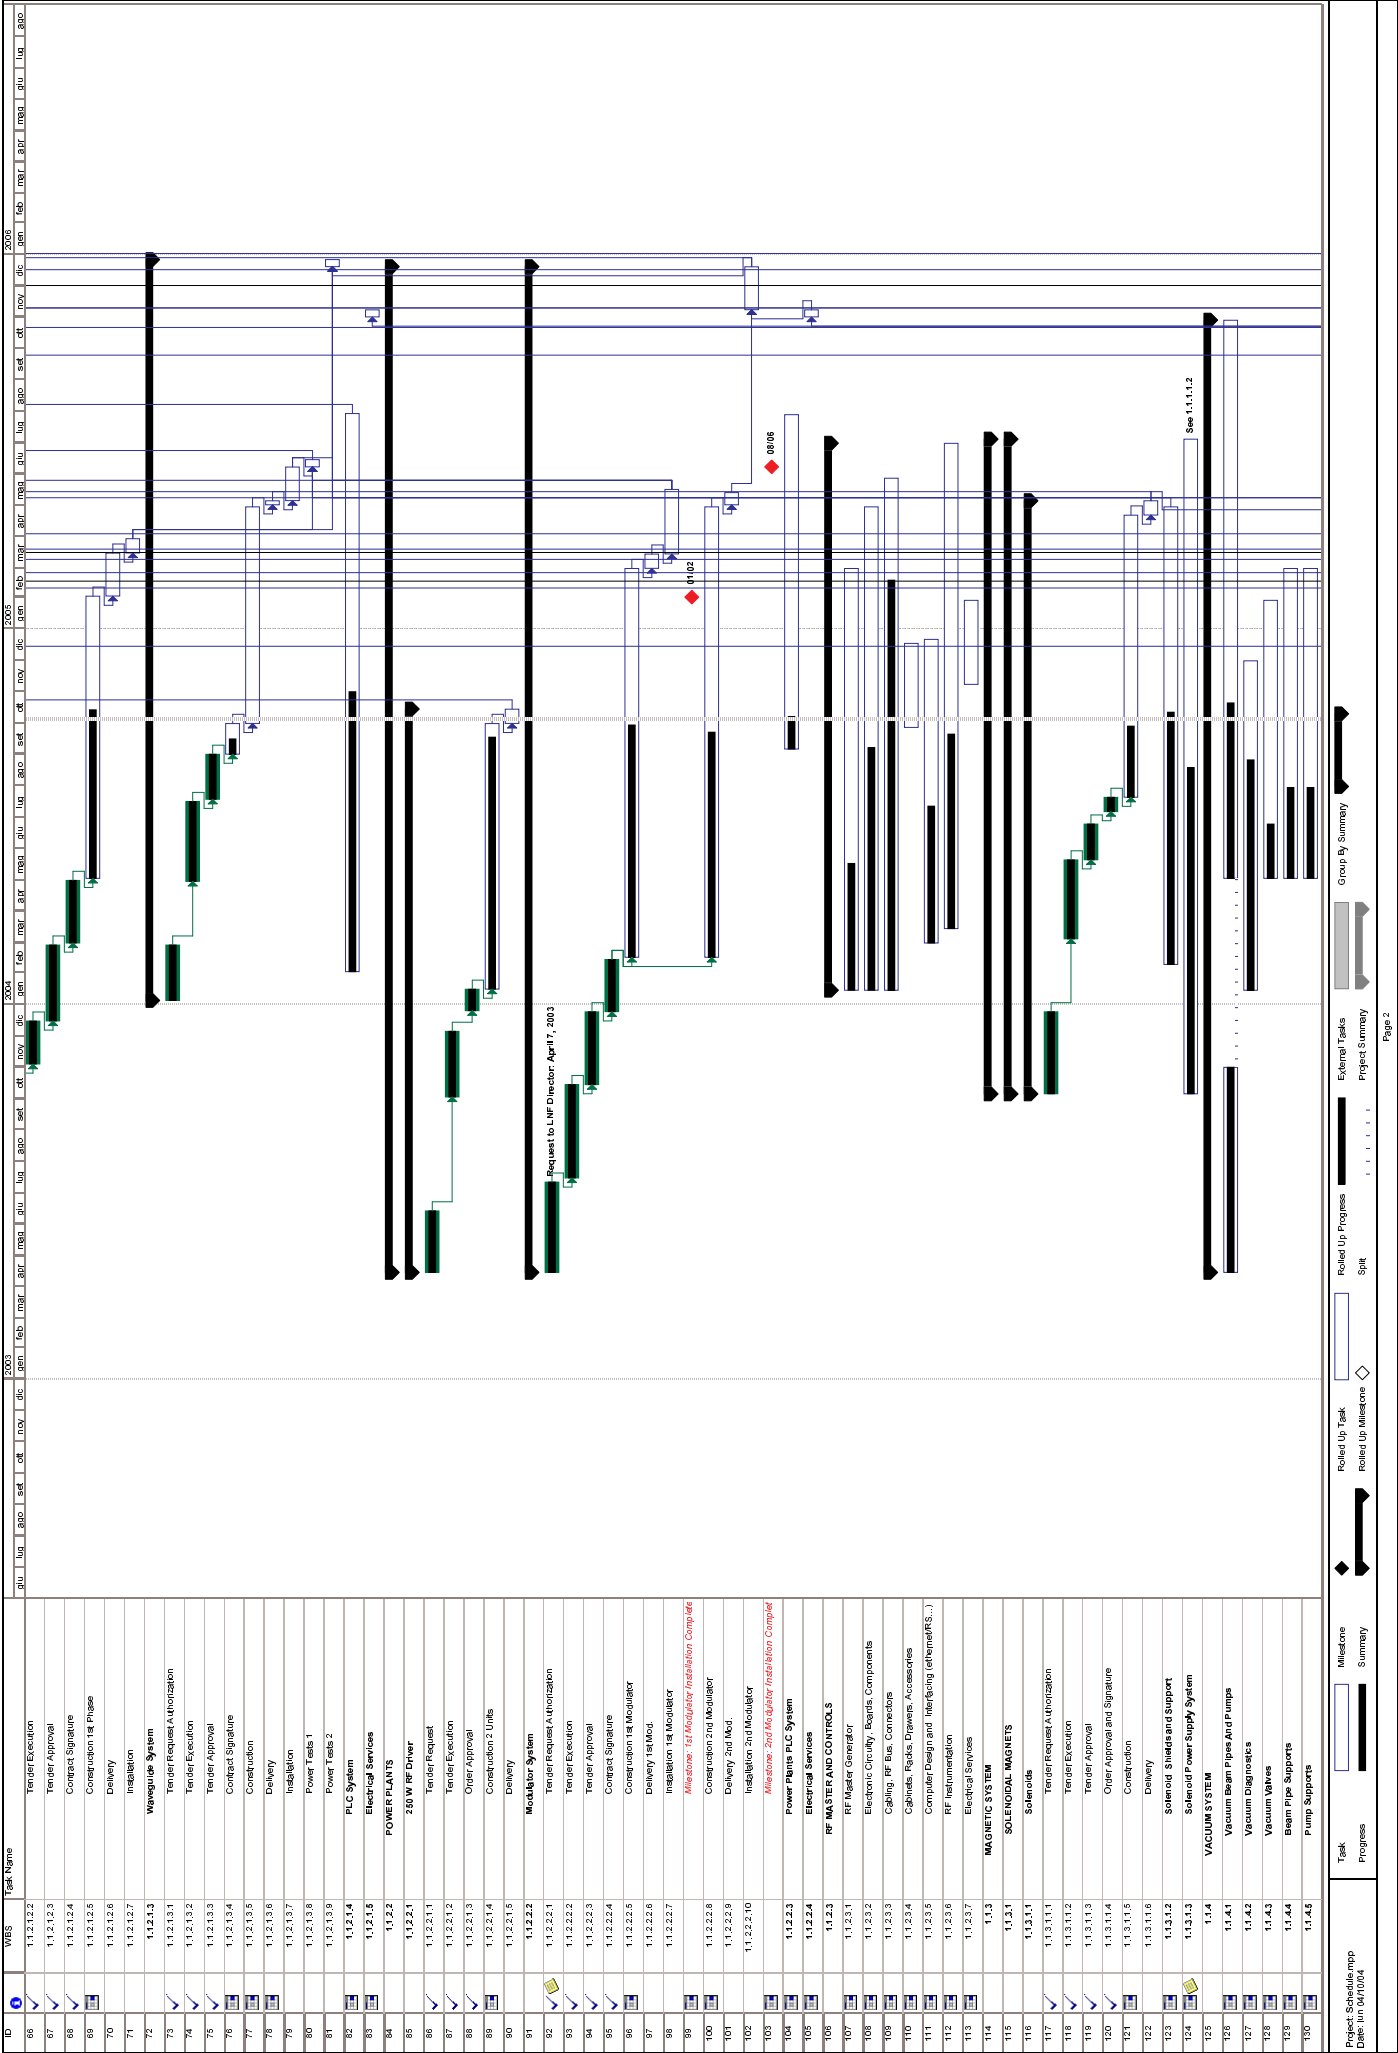
